


Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Project: Airport Lost Luggage Claim & Tracking Portal

Varun Rao | SRN: PES1UG24CS520 | Section I

1. Epics and User Stories


The Lab 1 functional requirements were broken down into 4 Epics and 8 User Stories in Jira, covering claim filing, identity verification, baggage matching and tracking, agent claim management, and passenger notifications.

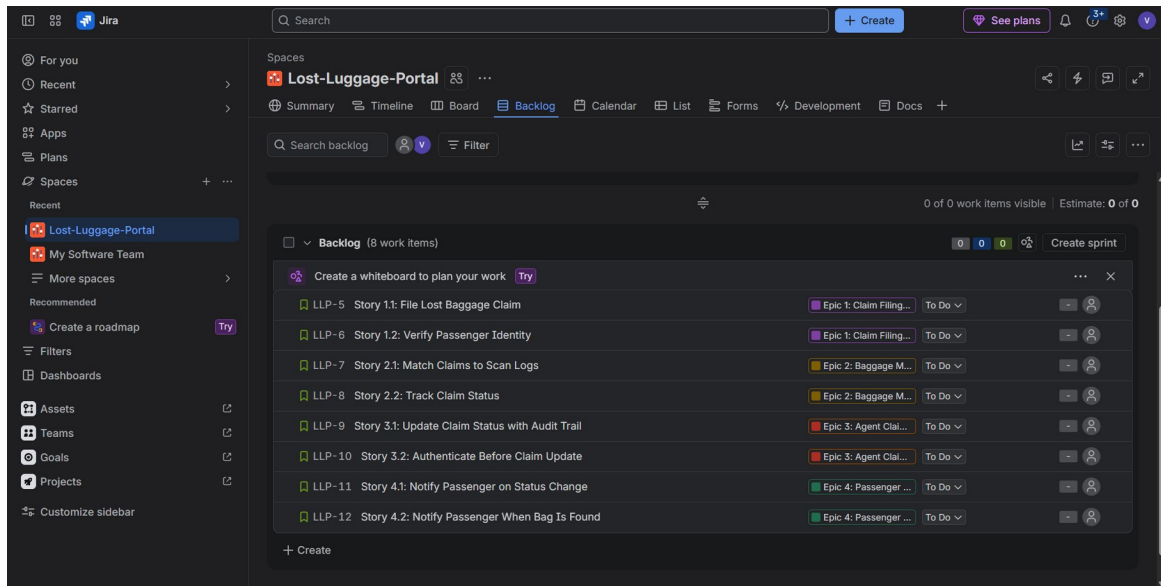

Backlog view showing all 4 Epics and 8 User Stories

2. Story Point Assignments


Story points were assigned to each User Story on the Fibonacci scale, based on relative complexity. Total backlog estimate: 31 points across 8 stories.

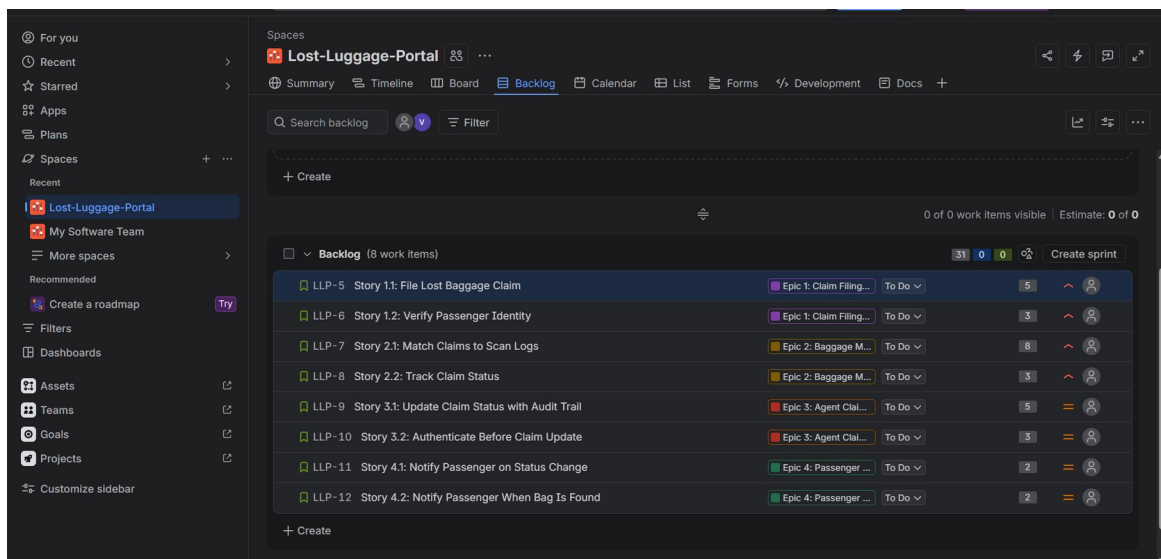

Backlog view showing story point and priority assignments

3. Sprint Board


Two sprints were run. Sprint 1 (LLP Sprint 1) covered Epics 1 and 2 (19 points); Sprint 2 (LLP Sprint 2) covered Epics 3 and 4 (12 points). The snapshot below shows Sprint 1 mid-progress, with items distributed across To Do, In Progress, and Done.

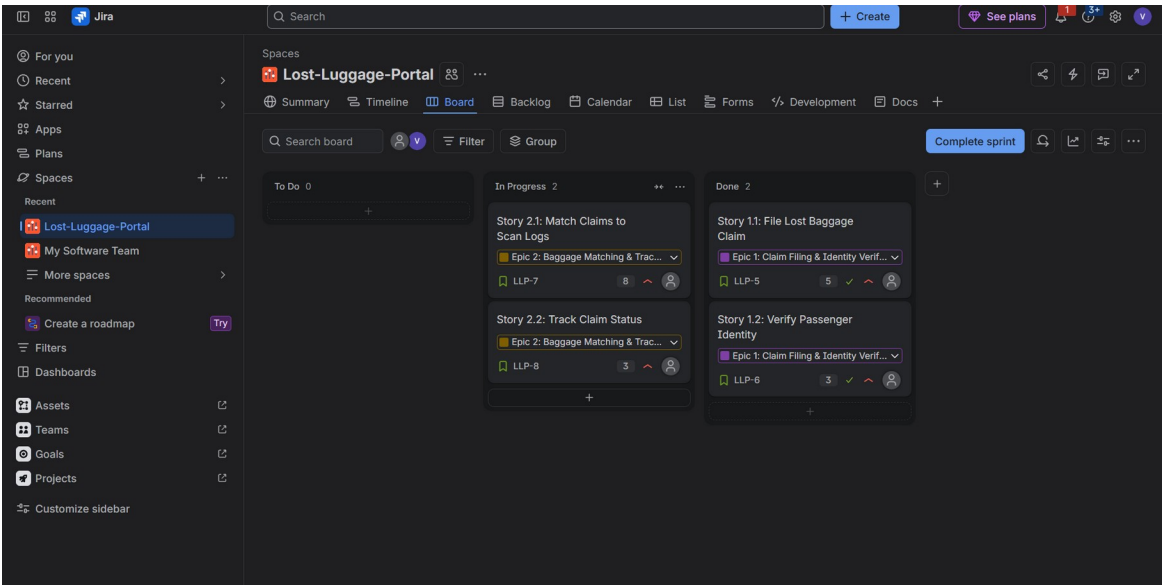

Active Sprint board (Sprint 1) showing tasks across To Do, In Progress, and Done


4. Burndown Charts

Sprint 1 ran from September 28 to October 5. The chart below shows a flat period before work began, followed by two step-drops as stories were completed in batches.

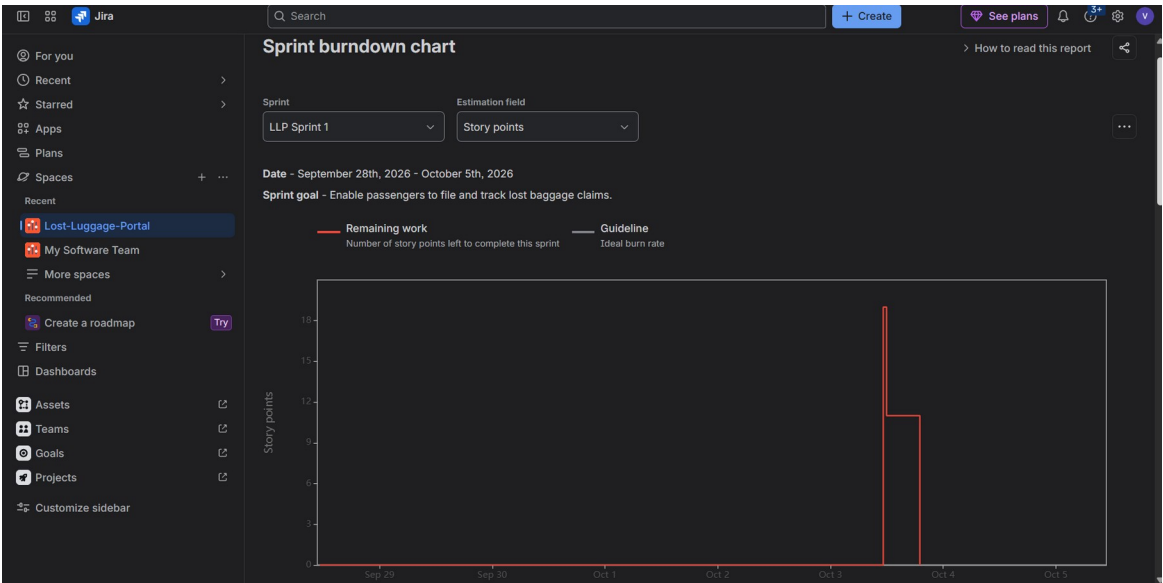

Burndown chart for Sprint 1

Sprint 2 ran from October 4 to October 12. Both stories batches were completed almost immediately after the sprint started, well ahead of the ideal guideline line.

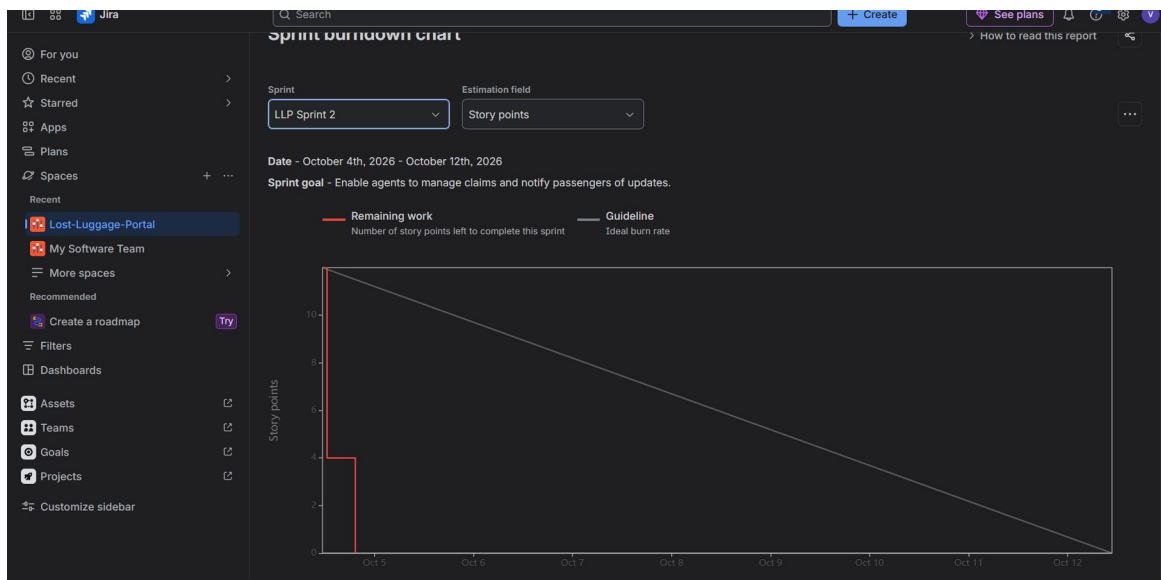

Burndown chart for Sprint 2

5. Reflection Questions

1. Did your estimations reflect the actual effort?

Mostly yes — we gave higher points to the stuff that was genuinely more complex, like matching claims to scan logs (8 pts), and lower points to simple lookups like tracking status (3 pts). Hard to fully validate since this was simulated and we didn't actually build the features, just estimated based on how complicated each one sounded.

2. Was your backlog well-prioritized?

Yeah, we think so. Claim filing, identity verification, and tracking status went into Sprint 1 as High priority since the whole system is useless without them. Agent-side claim updates and passenger notifications came in Sprint 2 as Medium priority, since they only matter once claims already exist in the system.

3. How did your simulated sprint align with your plan?

Both sprints finished 100% of what we planned — 19/19 points in Sprint 1, 12/12 in Sprint 2. We moved tasks in two batches each time (To Do → In Progress → Done) instead of spacing it evenly across the week, which is why the burndown chart shows sharp step-drops instead of a smooth daily decline.

4. What insights did the burndown chart give about your team's capacity?

Both charts show us finishing well ahead of the ideal guideline line, especially in Sprint 2 where all the points dropped off almost immediately. That's basically a sign we under-committed during planning — we could've pulled more stories into each sprint instead of leaving capacity on the table.
